COMPANY	SCHLUMBERGER WELL SERVICES	WELL	*ARAMCO 3-SR-24
FIELD	SAFANIYA	COUNTY	OFFSHORE
STATE	SAUDI ARABIA	LOCATION	1000'S & 1000'E FROM SE CORNER OF TRACT 24
SECT.	24	TWP.	17S
RGE.	32E	PERMANENT DATUM	GL
LOG MEASURED FROM	KB 25.0 FT ABOVE PERM. DATUM	ELEVATIONS	KB: 25.0 FT DF: 15.0 FT GL: 0.0 FT
DATE	31-AUG-1994	CASING	13 3/8" @ 1000.0 FT
RUN NUMBER	ONE	TD DRILLER	2000.0 FT
TD LOGGER	2000.0 FT	BTM. LOG INTERVAL	1999.0 FT
TOP LOG INTERVAL	0.0 FT	LOGGING SPEED	30.0 FT/MIN
DRILLER'S CASING DEPTH	1000.0 FT		
BIT SIZE	12 1/4 IN		
DRILL FLUID TYPE	GEL/LIGNO		
DRILL FLUID SAMPLE	FLOWLINE		
DRILL FLUID DENSITY	9.4 LB/GAL		
DRILL FLUID PH	9.3		
DRILL FLUID VISCOSITY	47.0 S		
DRILL FLUID FLUID LOSS	3.4 C3		
RM @ MEASURED TEMPERATURE	1.810 OHMM AT 68.0 DEGF		
RMF @ MEASURED TEMPERATURE	2.700 OHMM AT 68.0 DEGF		
RMC @ MEASURED TEMPERATURE	1.000 OHMM AT 68.0 DEGF		
RM @ BHT	1.829 OHMM AT 99.0 DEGF		
RMF @ BHT	1.935 OHMM AT 99.0 DEGF		
RMC @ BHT	1.833 OHMM AT 99.0 DEGF		
TIME CIRC. STOPPED	0800 8-30		
TIME LOGGER ON BTM.	2000		
MAX. REC. TEMP.	99.0 DEGF		
LOGGING UNIT NO.	8278		
LOGGING UNIT LOC.	SACRAMENTO		
RECORDED BY	ECKLEY/CHALLER		
WITNESSED BY	MLGER		

REMARKS:

INCREASINGLY FRESHER CONNATE WATER ABOVE 800'.
UNCONSOLIDATED SANDS PRODUCE LARGE INVASION PROFILES.
AFFECTING ILM. 2.5" x 4.0"-1.0"

EQUIPMENT NUMBERS:

DIS 1402	DIC 47	SLS RC 236	SLC FA 1589
MCM 1550	IEM BS 162	SLM BM 449	

ALL INTERPRETATIONS ARE OPINIONS BASED ON INFERENCES FROM ELECTRICAL OR OTHER MEASUREMENTS. WE CANNOT, HOWEVER, GUARANTEE THE ACCURACY OR CORRECTNESS OF ANY INTERPRETATIONS, AND WE SHALL NOT, EXCEPT IN THE CASE OF GROSS OR WILLFUL NEGLIGENCE ON OUR PART, BE LIABLE OR RESPONSIBLE FOR ANY LOSS, COSTS, DAMAGES OR EXPENSES INCURRED OR SUSTAINED BY ANYONE RESULTING FROM ANY INTERPRETATION MADE BY ANY OF OUR OFFICERS, AGENTS OR EMPLOYEES. THESE INTERPRETATIONS ARE ALSO SUBJECT TO OUR GENERAL TERMS AND CONDITIONS AS SET OUT IN OUR CURRENT PRICE SCHEDULE.

CHANGED PARAMETERS:

NAME	VALUE	UNIT	DEPTH (F)	NAME	VALUE	UNIT	DEPTH (F)
IFAM	1750000		300.5				

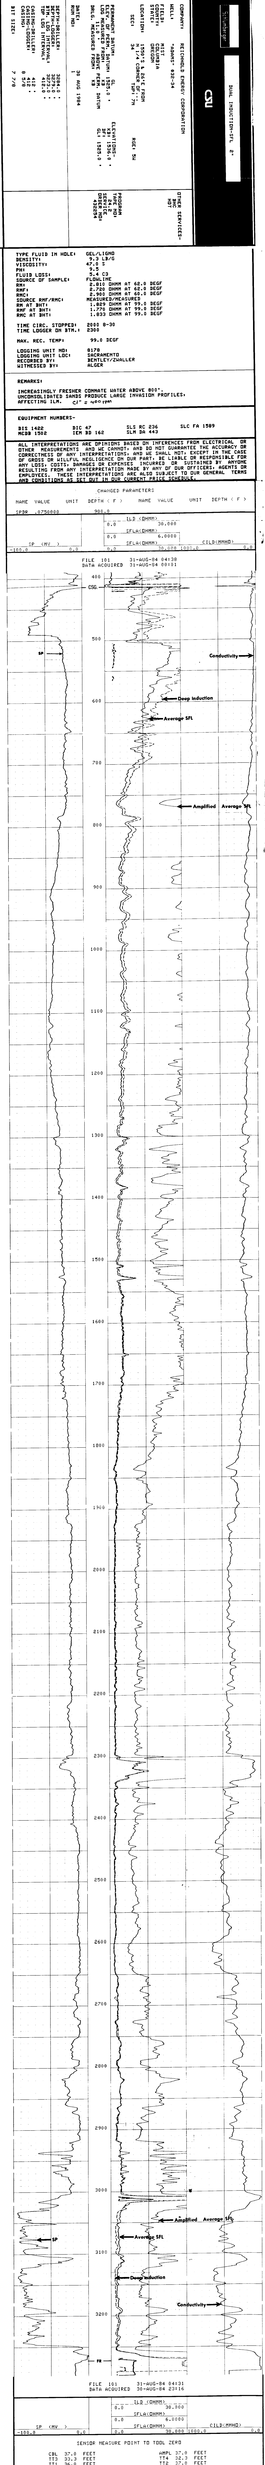

SENSOR MEASURE POINT TO TOOL ZERO

CBL	37.0	FEET	AMPL	37.0	FEET
CS	34.5	FEET	TT1	34.5	FEET
TT3	34.5	FEET	TT4	34.5	FEET
CALI	34.5	FEET	GRAY	34.5	FEET
SP	3.4	FEET	IFL	3.4	FEET
LL	2.5	FEET	ILM	2.5	FEET
SFLU	2.5	FEET	SFAM	2.5	FEET
MSFL	29.8	FEET			

PARAMETERS:

NAME	VALUE	UNIT	NAME	VALUE	UNIT
WOVI	WF1		BHT	16	
BITN	3	US	BBL	200	US
CDTS	185.000		BHCO	50	
TIME	1.0000	US/F	DFD	9.4000	LB/F
IDW	1.0000	OHMM	DFRC	2.0000	MMHO
FPHI	DPHI		MTEC	4.9000	MMHO
FRM	2.0000		MTEM	68.0	
SF	0.0750	IN	BS	12.25	
TEMP	68.0		DO	0.0	F
FF	NONE				
